



Ridgewood Pool EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

5109 Barton Rd • Madison, WI 2.17.2023

What's New?

As Spring is quickly approaching crews have been making a strong push on both the interior and exterior of the pool house in preparation for the upcoming site finishes.

Interior concrete slab on grade, masonry walls, in-wall and overhead rough-ins are now complete. Painting is also well underway as crews just finished out the mechanical, equipment, and snack shack rooms. The mechanical and equipment spaces will soon have both pool and plumbing equipment installed. Windows and storefront openings are now complete, and the exterior siding kicked off this week. Soon the exterior of the building will be complete, and the pool house will have its new look!

The first of the two surge tanks has also been set, allowing the pool piping from the dive vessel and new competition/recreation pool to be ran into the pool equipment pit for future connections and start-up.

The Past Few Weeks

- Concrete slab on grade at the pool house
- Interior non-loadbearing masonry walls and MEP rough-ins
- Painting of masonry walls at equipment and mechanical rooms
- Exterior furring, building wrap, and windows
- Setting of the first pool surge tank

Looking Ahead

- Ceiling framing for hard lid ceilings
- Painting of masonry walls and hard lid ceilings
- Exterior siding and trim
- Pool and plumbing equipment install
- Setting of the final surge tank



Above is a photo taken from the front entry of the new pool house. Soon the ceiling will be installed, walls painted, and cabinets set in place!

Below is a photo showing the first of the two surge tanks being set. This tank weighed almost 60,000 pounds!



DID YOU KNOW?

Between the four pool vessels (existing lap pool, dive vessel, competition/recreation pool, and wading pool), there will be over 448,000 gallons of water in the vessels. If these vessels were to be filled with a garden hose, that typically pumps at 12 gallons per minute, it would take over 25 days to fill all four vessels!

Questions?

Project Manager, Luke Kiefer / 608.358.4105 / lkiefer@findorff.com

Findorff
BUILDING & BEYOND




Ridgewood Pool EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

5109 Barton Rd • Madison, WI PAGE 2



Above: Pool piping coming from the surge tank for the dive vessel and new competition/recreation pool is now complete and has been stubbed into the pool house for future connections.

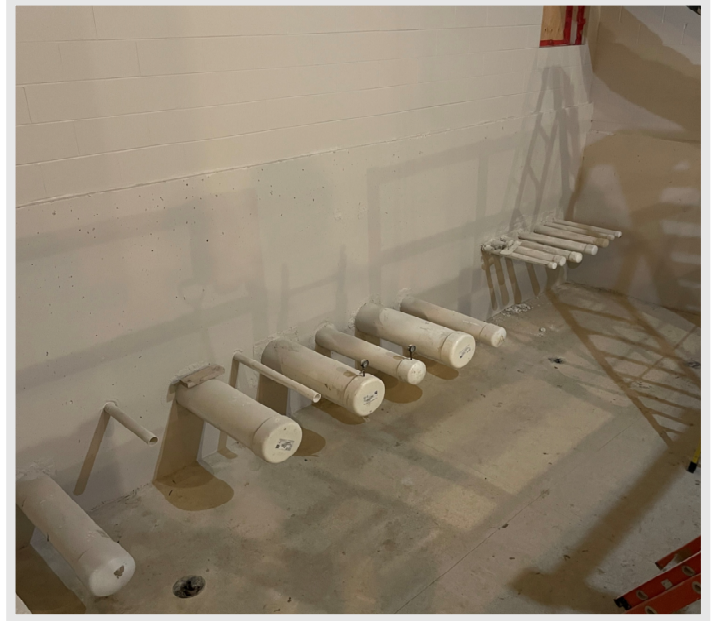

Above: A photo of the pool piping shown in the image to the left continuing into the pool house. These pipes will soon be connected to the pool equipment within the equipment room.



Above: A photo taken from the southwest corner of the pool house showing the building wrap, furring, and windows completely installed. Up next is the exterior window trim and siding!

Questions?

Project Manager, Luke Kiefer / 608.358.4105 / lkiefer@findorff.com

Findorff
BUILDING & BEYOND
